

Erosion and Sediment Control Schedule

Ingress—Egress
A stone access drive complete with under lying geo—textile fabric (20 feet wide and 50 feet long) for ingress and egress at the site shall be installed. This drive shall be the only entrance and exit to the site.

Silt Fence
A silt fence shall be installed prior to any earthwork activities at the site in the locations shown on the site plan as well as along the front of any lot that slopes towards the street.


Temporary Seeding
Disturbed areas of the site that are to remain idle for more than twenty—one(21) days shall be properly seeded and straw mulched within seven(7) days of completion of intitlal grading.

Temporary seeding and mulching as a thirty(30) foot strip of the entire front of the lot shall be maintained on the site once initial grading is complete.


Stabilization of critical areas within fifty(50) feet of any stream or wetland shall be complete within two(2) days of the disturbance if the site is to remain inactive for longer than fourteen(14) days.

Mulching
Straw—mulch shall be applied at a rate of 1 bale per every ten
(10) feet of curb, at a width of thirty(30) feet to the entire
length of the lot. Wood chips may also be used but must be
spread at a minimum depth of four inches over the thirty—foot
width and must be accompanied by a properly installed silt

Maintenance
Erosion and sediment controls shall be inspected every seven(7)
days or within 24 hours of a 0.5" or greater rainfall event.
Necessary repairs shall be made at this time.

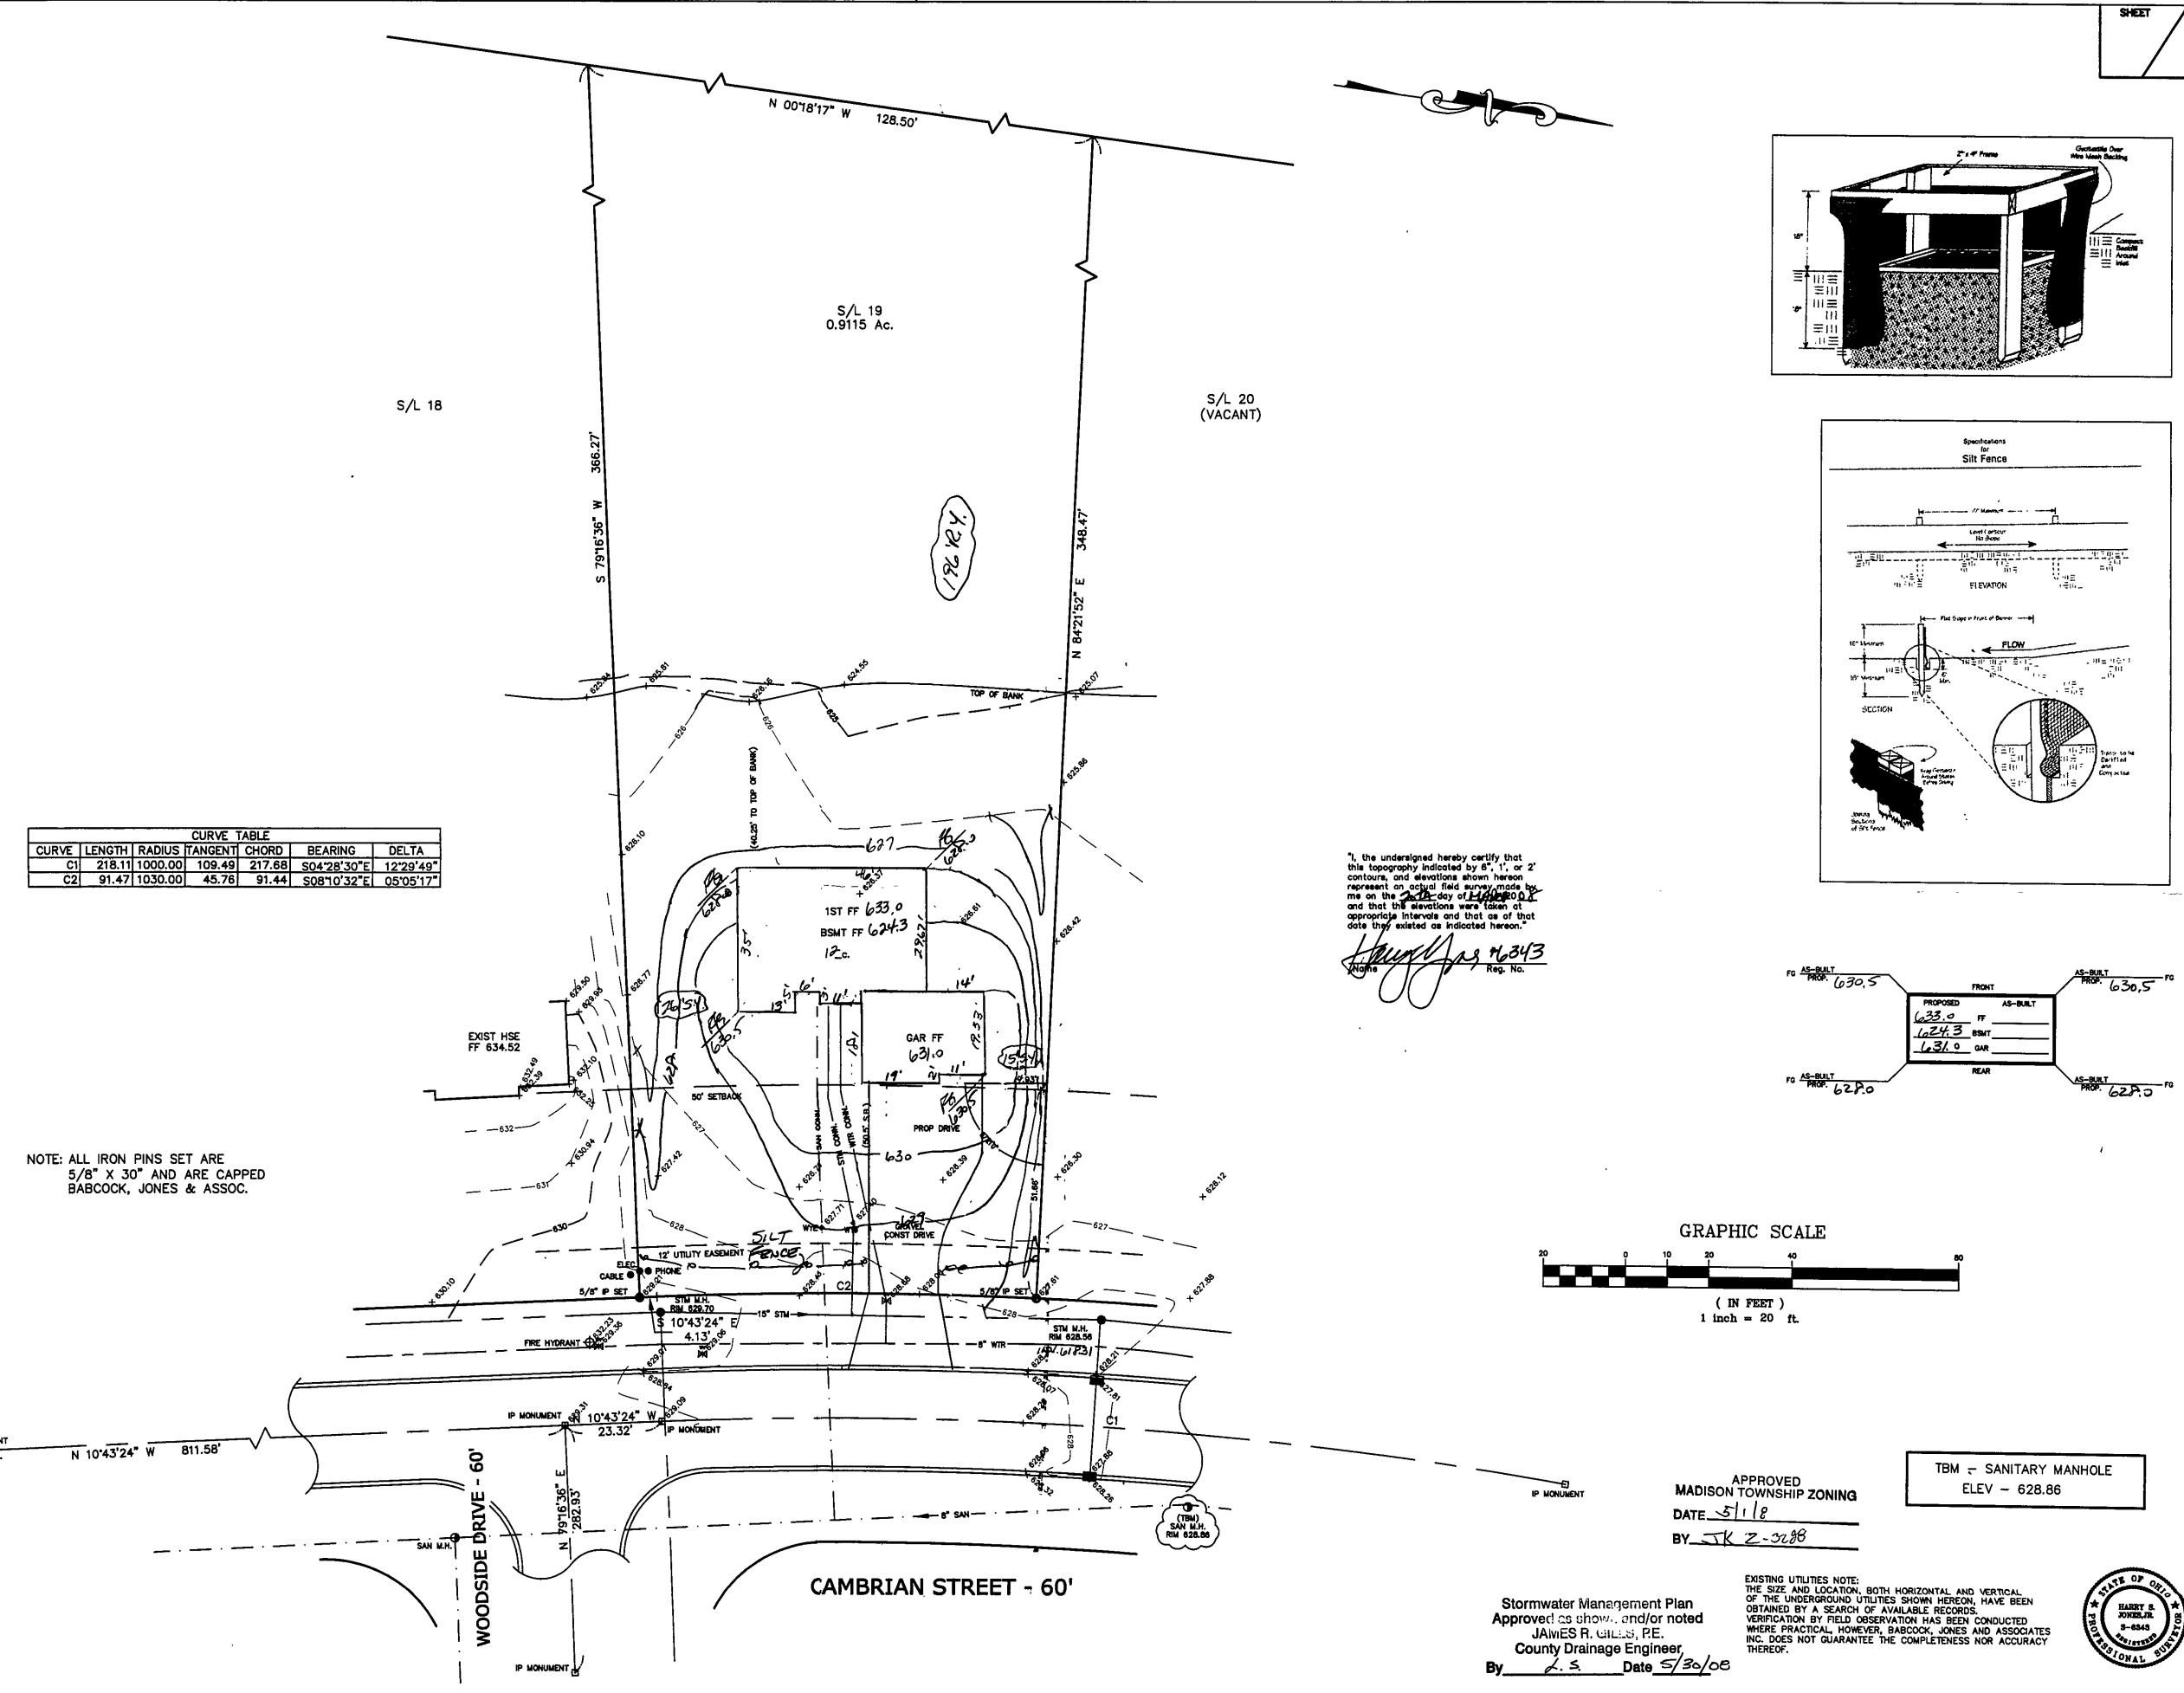

REV NO.	DESCRIPTION	DATE	BY	CHKD
l	REVISED SIDEYAND TO 15'	5/1/08	119	110
<u> </u>				



	DATE	04/21/08	
	DESIGN BY	H.J.	
•	DRAWN BY	B.P.]
	APPROVED BY	H.J.]
	CREW CHIEF	D	1.

SITE PLAN FOR CAPUTO

1"=20' JOB NO 05-138-19

PAINESVILLE OHIO 44077

S/L 19 CAMBRIAN STREET (MADISON MEADOWS SUB) MADISON TOWNSHIP LAKE COUNTY STATE OF OHIO

- - -
