

SEQUENCE OF CONSTRUCTION  
(S.R. 2 STAGE 1)

STAGE 1, PHASE B, STEP 3 CONSTRUCTION


1. CONSTRUCT STAGE 1, PHASE B, STEP 3 MAINTENANCE OF TRAFFIC.
2. REMOVE PORTIONS OF EXISTING SUPERSTRUCTURE, PIER AND APPROACH SLABS.
3. CONSTRUCT PORTIONS OF TEMPORARY SHORING.
4. REMOVE PORTIONS OF EXISTING ABUTMENTS.
5. COMPLETE CONSTRUCTION OF TEMPORARY SHORING.
6. EXCAVATE FOR MSE WALL BACKFILL.
7. INSTALL STAGE 1, PHASE B, STEP 3 ABUTMENT PILES.
8. CONSTRUCT STAGE 1, PHASE B, STEP 3 MSE WALL WITH TEMPORARY FACING.
9. CONSTRUCT STAGE 1, PHASE B, STEP 3 ABUTMENTS.
10. CONSTRUCT STAGE 1, PHASE B, STEP 3 PIER.
11. CONSTRUCT STAGE 1, PHASE B, STEP 3 SUPERSTRUCTURE.

STAGE 1, PHASE B, STEP 4 CONSTRUCTION

1. CONSTRUCT STAGE 1, PHASE B, STEP 4 MAINTENANCE OF TRAFFIC.
2. REMOVE REMAINING SUPERSTRUCTURE.
3. REMOVE REMAINING SUBSTRUCTURE.
- # S.R. 2 STAGE 2, PHASE B MAY BEGIN.
4. EXCAVATE FOR MSE WALL BACKFILL AND REMOVE TEMPORARY SHORING
5. CONSTRUCT STAGE 1, PHASE B, STEP 4 MSE WALL.
6. CONSTRUCT STAGE 1, PHASE B, STEP 4 ABUTMENTS.
7. CONSTRUCT STAGE 1, PHASE B, STEP 4 PIER.
8. CONSTRUCT STAGE 1, PHASE B, STEP 4 SUPERSTRUCTURE.

NOTES

1. FOR ADDITIONAL PHASE CONSTRUCTION DETAILS SEE SHEETS 7/47 AND 8/47.
2. FOR LIST OF ABBREVIATIONS, SEE SHEET 3/47.

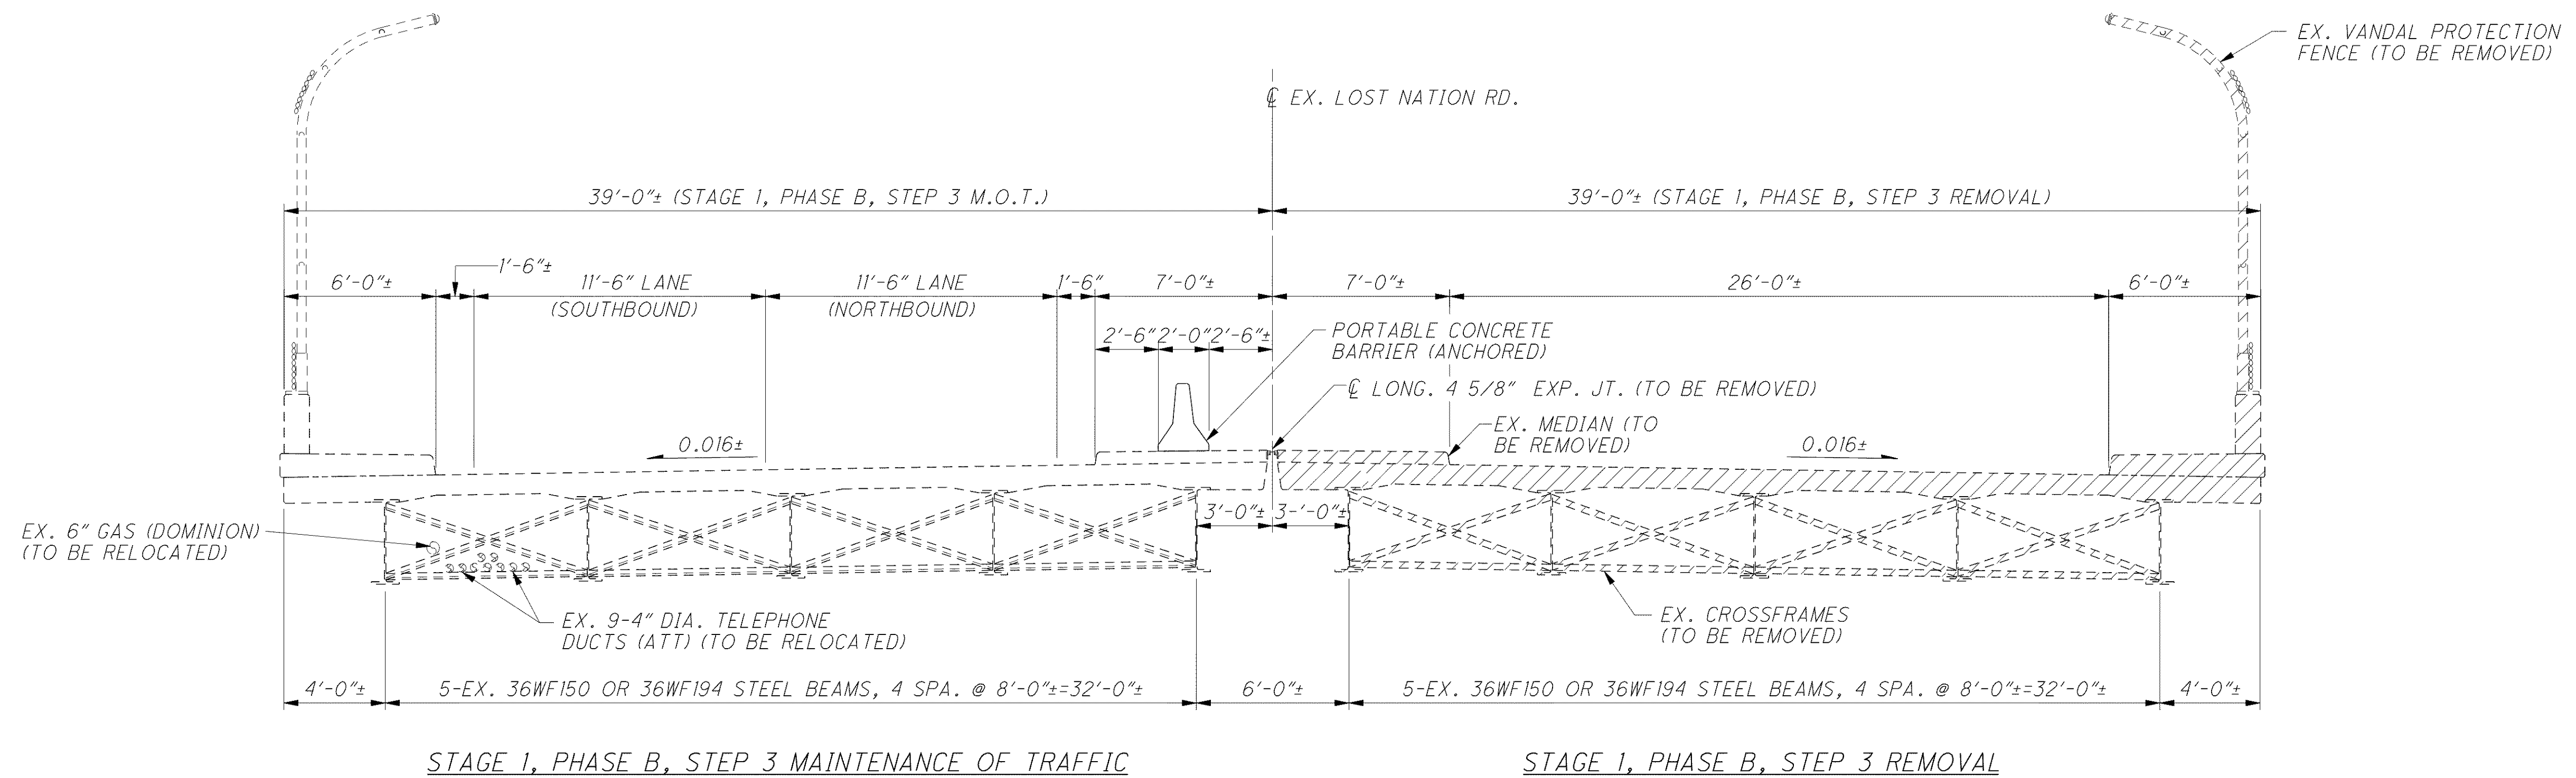

g:\project\cv000048a001\drawing\lak\13486\bridge\02\_0542c\sheets\02\_0542CPC001.dgn 6/24/2008 4:59:35 PM troxberry
