REVISIONS



Confrol Plan Sediment R COVE PAINESVIL SHORES PH. 3 VO Erosion and SIL 239 OUTRIGGER OF LAKE ERIE S

WSÖ CHECKER DWN DEC. 15, 2005 04114-239

TEMPORARY SEEDING SPECIFICATIONS SEEDING DATES **SPECIES** LB./1000 FT. PER AC MARCH 1 TO AUGUST 15 OATS 3 4 BUSHEL TEMPORARY SEEDING TALL FESCUE 40 LB. AND MULCHING ANNUAL RYEGRASS 40 LB. PERENNIAL RYEGRASS 40 LB. **TALL FESCUE** 40 LB. **ANNUAL RYEGRASS** 40 LB. **AUGUST 16 TO NOVEMBER 1** RYE 2 BUSHEL **TALL FESCUE** 1 40 LB. **ANNUAL RYEGRASS** 1 40 LB. WHEAT 3 2 BUSHEL **TALL FESCUE** 40 LB. ANNUAL RYEGRASS 40 LB. PERENNIAL RYEGRASS 40 LB. TALL FESCUE 40 LB. **ANNUAL RYEGRASS** 40 LB. **NOVEMBER 1 TO SPRING SEEDING** USE MULCH ONLY, SODDING PRACTICES OR DORMANT SEEDING NOTE: OTHER APPROVED SEED SPECIES MAY BE SUBSITUTED

EROSION AND SEDIMENT CONTROL SCHEDULE **INGRESS-EGRESS**

A STONE ACCESS DRIVE COMPLETE WITH UNDER LYING GEO-TEXTILE FABRIC (20 FEET WIDE AND 50 FEET LONG) FOR INGRESS AND EGRESS AT THE SITE SHALL BE INSTALLED. THIS DRIVE SHALL BE THE ONLY ENTRANCE AND EXIT TO THE SITE.

SILT FENCE

Z

LITTLE MOUNTAIN HOMES,

ALL SILT FENCE SHALL BE INSTALLED PRIOR TO ANY EARTHWORK ACTIVITIES AT THE SITE IN THE LOCATIONS SHOWN ON THE SITE PLAN AS WELL AS ALONG THE FRONT OF ANY LOT THAT SLOPES TOWARDS THE STREET

DISTURBED AREAS OF THE SITE THAT ARE TO REMAIN IDLE FOR MORE THAN THIRTY (30) DAYS SHALL BE PROPERLY SEEDED AND STRAW MULCHED WITHIN SEVEN (7) DAYS OF COMPLETION OF INITIAL GRADING. TEMPORARY SEEDING AND MULCHING OF A THIRTY (30) FOOT STRIP OF THE ENTIRE FRONT OF THE LOT SHALL BE MAINTAINED ON THE SITE ONCE INITIAL GRADING IS

STABILIZATION OF CRITICAL AREAS WITHIN FIFTY (50) FEET OF ANY STREAM OR WETLAND SHALL BE COMPLETE WITHIN TWO (2) DAYS OF THE DISTURBANCE IF THE SITE IS TO REMAIN INACTIVE FOR LONGER THAN FOURTEEN (14) DAYS.


STRAW-MULCH SHALL BE APPLIED AT A RATE OF 1 BALE PER EVERY TEN (10) FEET OF CURB, AT A WIDTH OF THIRTY (30) FEET OF THE ENTIRE LENGTH OF THE LOT. WOOD CHIPS MAY ALSO BE USED BUT MUST BE SPREAD AT A MINIMUM DEPTH OF FOUR INCHES OVER THE THIRTY-FOOT WIDTH AND MUST BE ACCOMPANIED BY A PROPERLY INSTALLED SILT FENCE.


MAINTENANCE

EROSION AND SEDIMENT CONTROLS SHALL BE INSPECTED EVERY SEVEN (7) DAYS OR WITHIN 24 HOURS OF A 0.5" OR GREATER RAINFALL EVENT. NECESSARY REPAIRS SHALL BE MADE AT THIS TIME.

ALL EROSION AND SEDIMENT CONTROL SPECIFICATIONS, APPLICATIONS, AND TIMETABLES ARE BASED OF THE DESCRIPTIONS AND STANDARDS OF THE OHIO DEPARTMENT OF NATURAL RESOURCES "RAINWATER AND LAND DEVELOPMENT MANUAL" AND CAN BE FOUND IN THE LAKE COUNTY EROSION AND SEDIMENT CONTROL RULES AS ADOPTED DECEMBER 21, 1999.

THE SPECIFIED EROSION AND SEDIMENT CONTROL STANDARDS ARE GENERAL GUIDELINES AND SHALL NOT LIMIT THE RIGHT OF THE COUNTY TO IMPOSE, AT ANY TIME, ADDITIONAL, MORE STRINGENT REQUIREMENTS. NOR SHALL THE STANDARDS LIMIT THE RIGHT OF THE COUNTY TO WAIVE, IN WRITING, INDIVIDUAL REQUIREMENTS. 04114-239



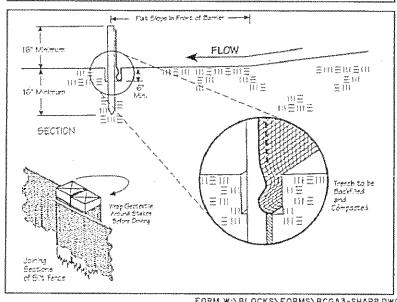

FORM W:\BLOCKS\FORMS\BCGA3-SHARP.DW
