

# Foresight Engineering Group



Engineers & Surveyors

40-225-100  
40-225-100  
40-225-100  
40-225-100

LARIMAR LAKEFRONT NEIGHBORHOOD  
SUBLOT 9  
City of Willowick – Lake County – Ohio  
Erosion & Sediment Control Notes

SHEET NO.

2/2

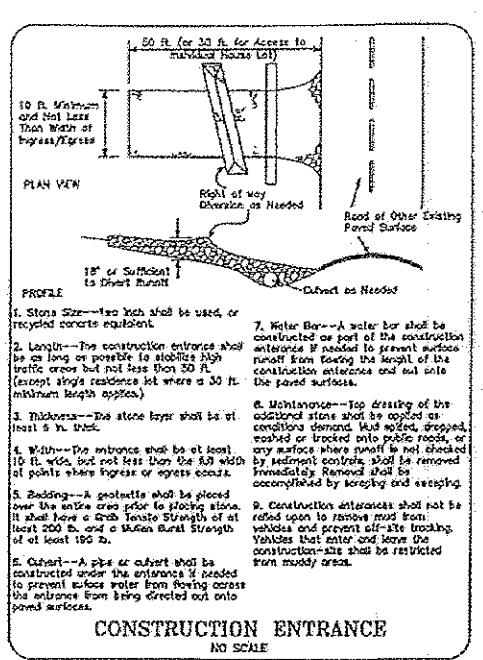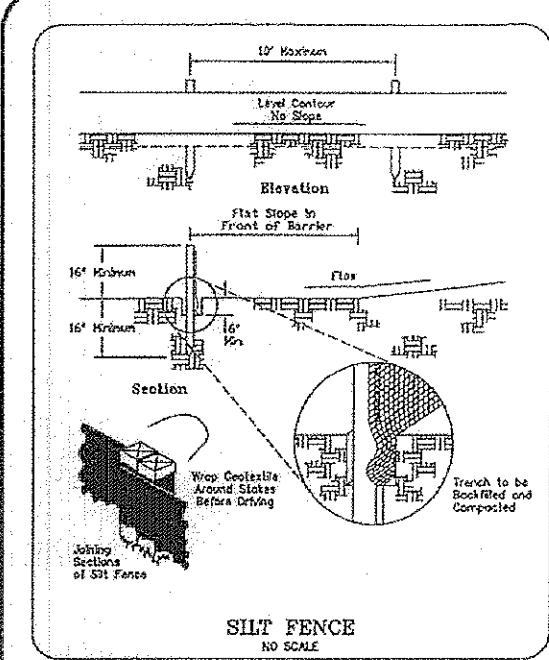

#### GENERAL EROSION AND SEDIMENT CONTROL NOTES:

Erosion control shall consist of temporary control measures as detailed on the plans or ordered by the governing agency during the life of the contract to control soil erosion and sedimentation through use of erosion control best management practices (BMP's).

Sediment control shall be accomplished by seeding and mulching all disturbed areas immediately upon completion of excavation or fill and finish grading in accordance with specifications of the CONR Rainwater and Land Development Manual.

Temporary erosion and sediment control items, the location and size of which are detailed on the plans, shall be installed by the contractor prior to commencement of any clearing or earthwork operations. Conditions that develop during construction that were not foreseen during design stage; that require additional or modified temporary or permanent BMP's shall be approved by the design engineer and reflected on the revised Water Management and Sediment Control Plan.

Erosion and sediment controls shall be implemented as the first step of grading and within 7 days from the start of grubbing. Upon completion of construction, seeding and mulching shall immediately follow to aid in the stabilization and minimize erosion and sediment. All erosion and sediment controls shall continue to function until disturbed areas are re-stabilized.

Other erosion and sediment control items may be necessary due to environmental conditions and may be required at the discretion of the City of Willowick or its representatives.

#### STABILIZATION

Site stabilization either permanent or temporary must follow the requirements as applicable on the following tables:

TABLE 1: PERMANENT STABILIZATION

Area requiring permanent stabilization	Time frame to apply erosion control
Any area that will lie dormant for one year or more	Within seven days of the most recent disturbance
Any area within 50 ft. of a stream and at final grade	Within two days of reaching final grade
Any other areas at final grade	Within seven days of reaching final grade within that area

TABLE 2: TEMPORARY STABILIZATION

Area requiring temporary stabilization	Time frame to apply erosion control
Any disturbed areas within 50 ft. of a stream and not at final grade	Within two days of the most recent disturbance if the area will remain idle for more than 14 days
For all construction activities, any disturbed areas that will be dormant for more than 21 days but less than one year, and not within 50 ft. of stream	Within seven days of the most recent disturbance within the area  For residential subdivisions, disturbed areas must be stabilized at least seven days prior to transfer of permit coverage for the individual lot(s)
Disturbed areas that will be idle over winter	Prior to November 1 straw mulch 2 to 3 bales per 1000 sq.ft. and/or 2 tons per acre.

Note: Where vegetative techniques may cause structural instability or are otherwise unattainable, alternative stabilization techniques must be employed.

#### SEEDING AND MULCHING

##### Temporary Seeding Species Selection

Seeding Dates	Species	lb./1,000 ft.	Per Acre
March 1 to August 15	Oats	3	128 lb
	Tall Fescue	1	40 lb
	Annual Ryegrass	1	40 lb
	Perennial Ryegrass	1	40 lb
	Tall Fescue	1	40 lb
	Annual Ryegrass	1	40 lb
August 16 to November 1	Rye	3	112 lb
	Tall Fescue	1	40 lb
	Annual Ryegrass	1	40 lb
	Wheat	3	120 lb
	Tall Fescue	1	40 lb
	Annual Ryegrass	1	40 lb
	Perennial Ryegrass	1	40 lb
	Tall Fescue	1	40 lb
	Annual Ryegrass	1	40 lb
November 1 to Spring Seeding	Use mulch only, sodding practices or dormant seeding		

Note: Other approved seed species may be substituted

Seeding areas shall be inspected and where the seed has not produced 80% cover shall be reseeded as necessary by the contractor. Areas shall be stabilized with mulch when conditions prohibit seeding.

Straw mulching shall be applied at a rate 2-3 standard 45 lb. bales per 1000 sq.ft. of disturbed area or 2 tons per acre. All hydroseeding must be straw mulched according to the above specifications unless it is watered weekly.

All detention ponds, retention ponds, water quality structures, sediment ponds, sediment traps, earthen diversions or embankments shall be seeded and mulched within 7 days of completed construction.

Disturbed areas that will remain inactive for a period of 21 days or longer shall be stabilized with seeding and mulching or other appropriate means, within seven day after earth moving ceases. Permanent soil stabilization shall be installed within seven days after final grading is reached on any portion of the site.

Stabilize areas within fifty (50) feet of any wetland or stream, within two (2) days on all inactive disturbed areas that will remain inactive for fourteen (14) days or longer.

Permanent Seeding			
Seed Mix	Seeding Rate		Notes
	lb./ac	lb./1,000 ft.	
<b>General Use</b>			
Creeping Red Fescue	20-40	1/2-1	
Domestic Ryegrass	10-20	1/4-1/2	
Kentucky Bluegrass	10-20	1/4-1/2	
Tall Fescue	40	1	
Dwarf Fescue	40	1	
<b>Slope Banks or Cut Slopes</b>			
Tall Fescue	40	1	
Crown Vetch	10	1/4	
Tall Fescue	20	1/2	Do not seed later than August
Flat Pea	20	1/2	
Tall Fescue	20	1/2	Do not seed later than August
<b>Road Ditches and Swales</b>			
Tall Fescue	40	1	
Dwarf Fescue	90	2 1/4	
Kentucky Bluegrass	5		
<b>Lawns</b>			
Kentucky Bluegrass	60	1 1/2	
Perennial Ryegrass	60	1 1/2	
Kentucky Bluegrass	60	1 1/4	
Creeping Red Fescue	60	1 1/4	For shaded areas

Note: Other approved seed species may be substituted

REVISIONS:

SCALE: Horz. 1" = 200 ft.  
Vert. None

FILE NAME: 10601CoSite Plans Site Plan 9-130520.dwg, S:\\202\\2013\\11\\3545 AM, Copyright Foresight Engineering Group, Inc.

DATE: May 20, 2013
