


j:\LAK\13486\bridge\LAK002_0400C\sheets\02_0400CPC004.dgn 03-JUL-2008 1:37PM linfn

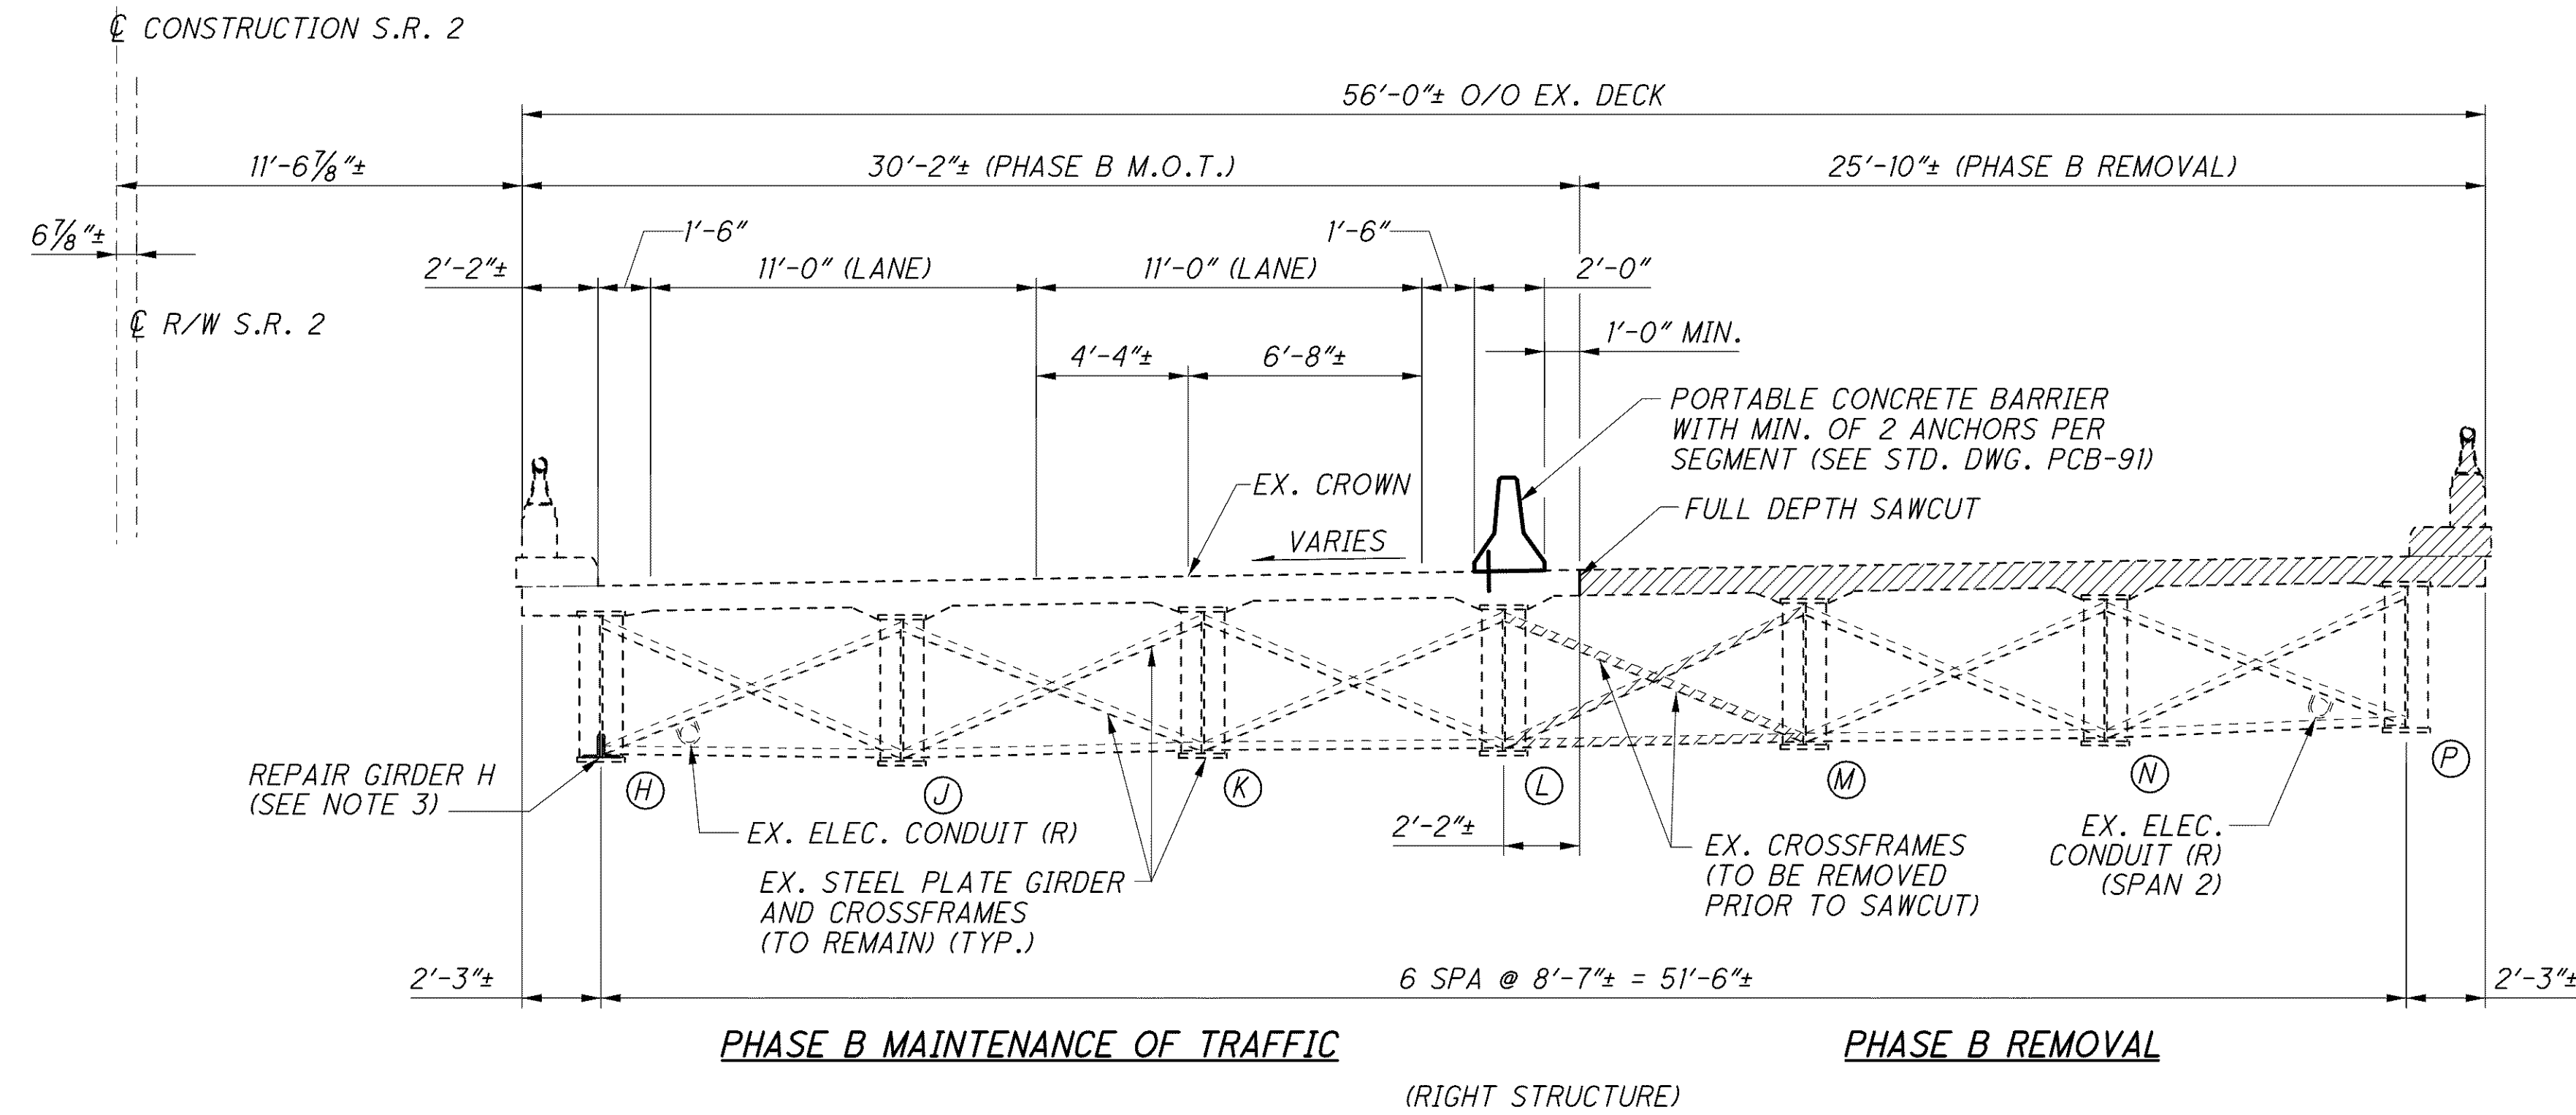


PHASE B BRIDGE CONSTRUCTION (RIGHT BRIDGE)

1. REPAIR GIRDER H. (SEE NOTE 3)
2. SETUP PHASE B MOT.
3. REMOVE EXISTING CROSSFRAMES BETWEEN GIRDERS L AND M.
4. SAW CUT AND REMOVE EXISTING OUTSIDE SECTION OF DECK AND PARAPET.
5. REMOVE PORTION OF ABUTMENT AND APPROACH SLAB.
6. BUILD ABUTMENT AND PIER EXTENSIONS.
7. ERECT GIRDERS 8 THRU 10 AND CROSSFRAMES.
8. PLACE ABUTMENT DIAPHRAGMS.
9. PLACE DECK AND PARAPETS.
10. SETUP FOR PHASE C MOT.

NOTES

1. PHASE A CONSTRUCTION CONSISTS OF THE ROADWAY MEDIAN SHOULDER RECONSTRUCTION TO EXISTING GRADES
2. FOR LIST OF ABBREVIATIONS, SEE SHEET 4/67.
3. GIRDER H REPAIR TO BE COMPLETED PRIOR TO PHASE B MOT SETUP. MEDIAN SHOULDER TO BE TEMPORARILY CLOSED DURING REPAIRS TO GIRDER H. FOR GIRDER H REPAIR DETAILS, SEE SHEET 45/67.
4. ALL PHASES REFERENCED ARE TO BE COMPLETED UNDER STAGE 3 SEQUENCE OF CONSTRUCTION, SEE MOT DRAWINGS.

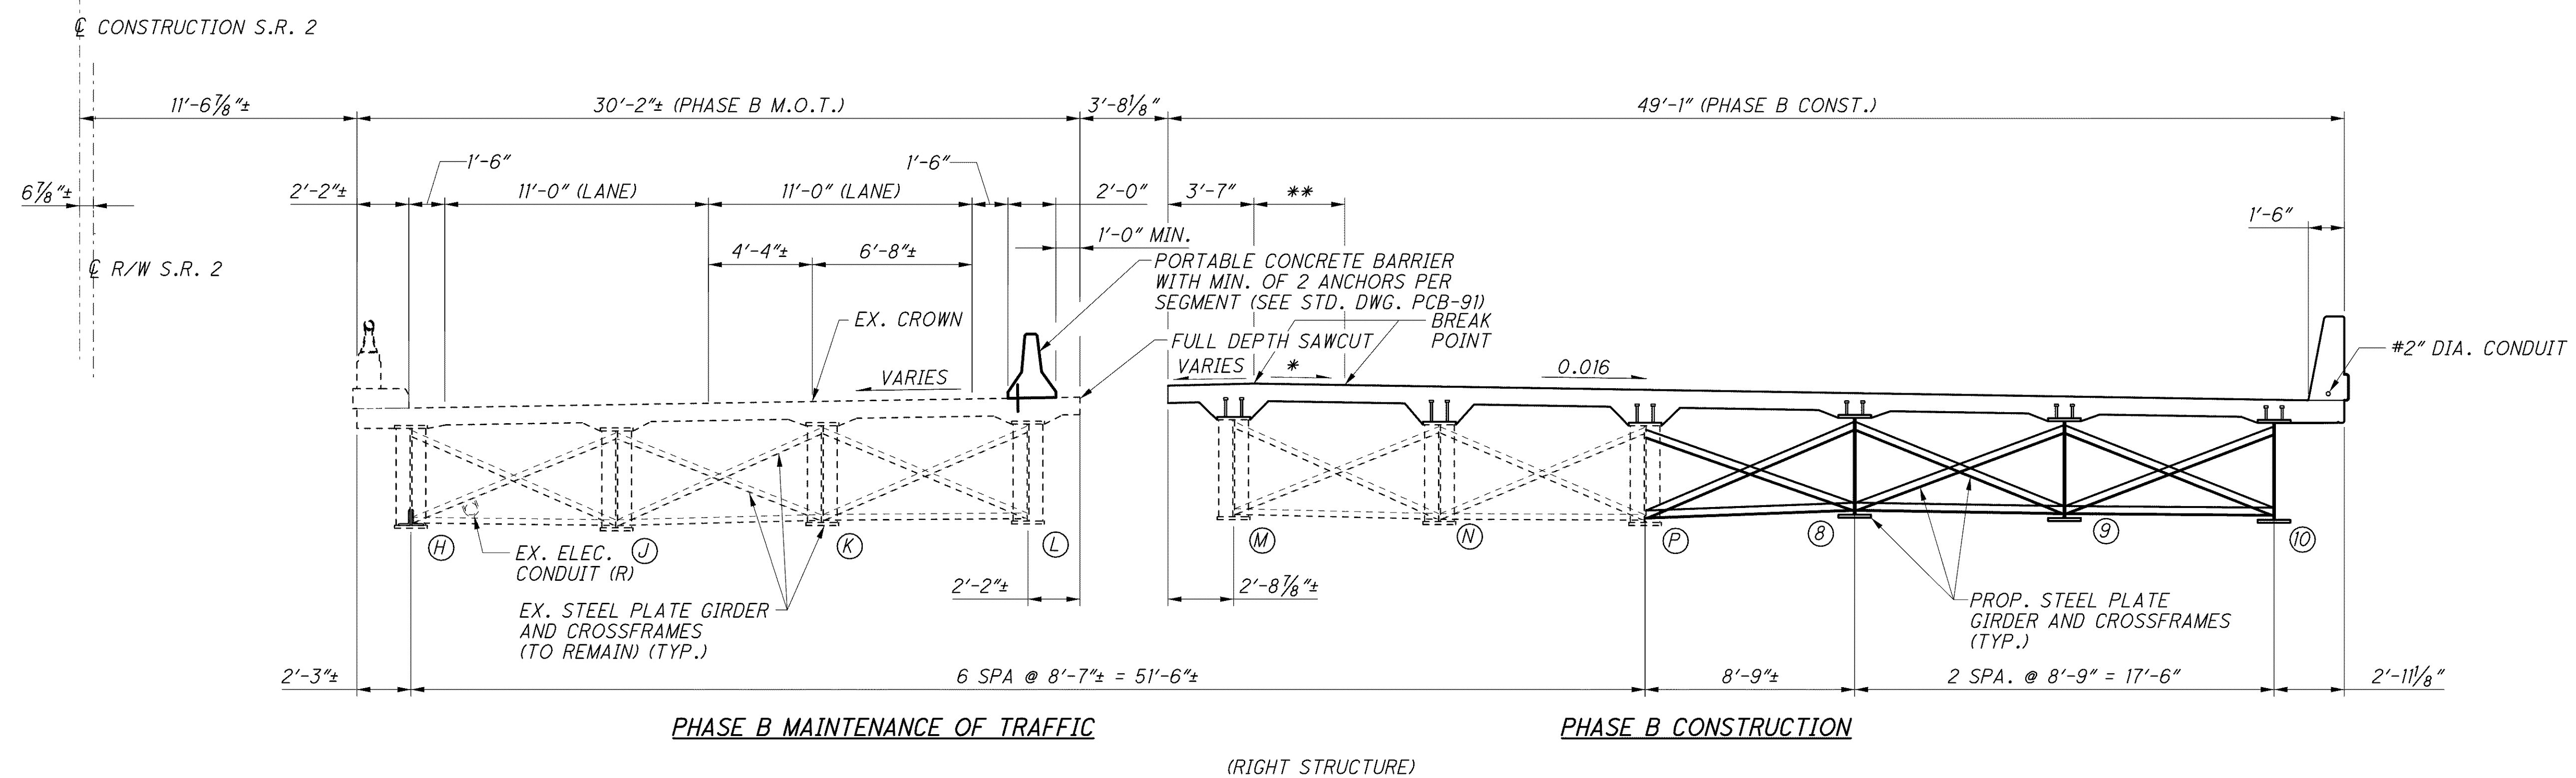

* VARIES FROM 0.014 AT STA. 311+03.03 TO 0.016 AT STA. 311+06.68
 ** VARIES FROM 0'-0" AT STA. 311+03.03 TO 3'-8 7/8" AT 311+06.68
 # FULL LENGTH OF BRIDGE

PHASED CONSTRUCTION DETAILS IV BRIDGE NO. LAK-2-0400 L&R STATE ROUTE 2 OVER VINE STREET	
LAK-2-3.32 PID 13486	DESIGN AGENCY PARSONS BRINCKERHOFF QUADE & DOUGLAS, INC. 614 W. SUPERIOR AVE., SUITE 400 CLEVELAND, OHIO 44113
DRAWN: NAL CHECKED: PWP DESIGNED: BMG	REVISIONS: NO. 1: RJO DATE: 6-19-08 STRUCTURE FILE NUMBER: 4300572(L) 4300602(R)
11 / 67	<div style="border: 1px solid black; border-radius: 50%; width: 30px; height: 30px; display: flex; align-items: center; justify-content: center;"> 1336 1679 </div>
